Lab 2: Agile Backlog Creation and Sprint Simulation in Jira

SRN: PES2UG24CS042 | Problem Statement #38 | Dropshipping Inventory & Order Orchestrator

1. What I built

I took the five functional requirements from Lab 1 and grouped them into four Epics. Under those I wrote ten User Stories in the As a / I want / So that format, and gave each one a priority and a story point estimate off the Fibonacci scale. I then split the ten across two sprints of a week each and ran both to completion on the Jira board.

Epic breakdown:

Epic	Lab 1 requirements covered	Stories	Points
Order Intake and Processing	FR-001, NFR-001	2	8
Supplier Stock and Purchase Orders	FR-001, FR-002	3	21
Exception and Stock Handling	FR-003, NFR-002	3	11
Tracking and Owner Dashboard	FR-004, FR-005	2	13

2. Reflection questions

Did your estimations reflect the actual effort?

I simulated the sprint instead of building anything, so there is no real effort to compare the estimates against. The relative sizing still looks right to me though. The 8 point stories are the ones that have to reach out to another system or take several steps to finish: checking supplier stock in real time, splitting a multi supplier order, and building the owner dashboard. The 3 point ones are much narrower, like verifying an HMAC signature or firing an alert. To really test any of this I would have to compare the estimates against hours actually spent, which this lab could not give me.

Was your backlog well-prioritized?

I think so. Every High priority story went into Sprint 1, and between them they cover the whole core order path: the webhook comes in, the system verifies it, checks stock, splits the order, and sends the purchase order out. Without those the system does nothing at all. The four Medium stories went into Sprint 2. Alerts, retries, tracking numbers and the dashboard all make the system better to live with, but an order can still reach a supplier without any of them. That is why they sat lower down the list.

How did your simulated sprint align with your plan?

SBoth sprints closed everything they took on, 34 points in the first and 19 in the second. Nothing carried over and nothing got added halfway through. That only happened because I was dragging cards across a board rather than writing code. A real sprint usually ends with something unfinished, or a blocker nobody saw during planning.

What insights did the burndown chart give about your team's capacity?

The line dropped straight down instead of stepping down across the week, because I moved everything to Done in one go. In practice a burndown falls in stages as the individual stories close. A drop that shape on a live project would make me suspect the stories were too big, or that people were only marking work Done right at the end instead of as they finished it. Across both sprints the velocity came to 53 points, which is the number you would plan a third sprint against. With one person and a simulated week it does not mean much yet.

3. Screenshots

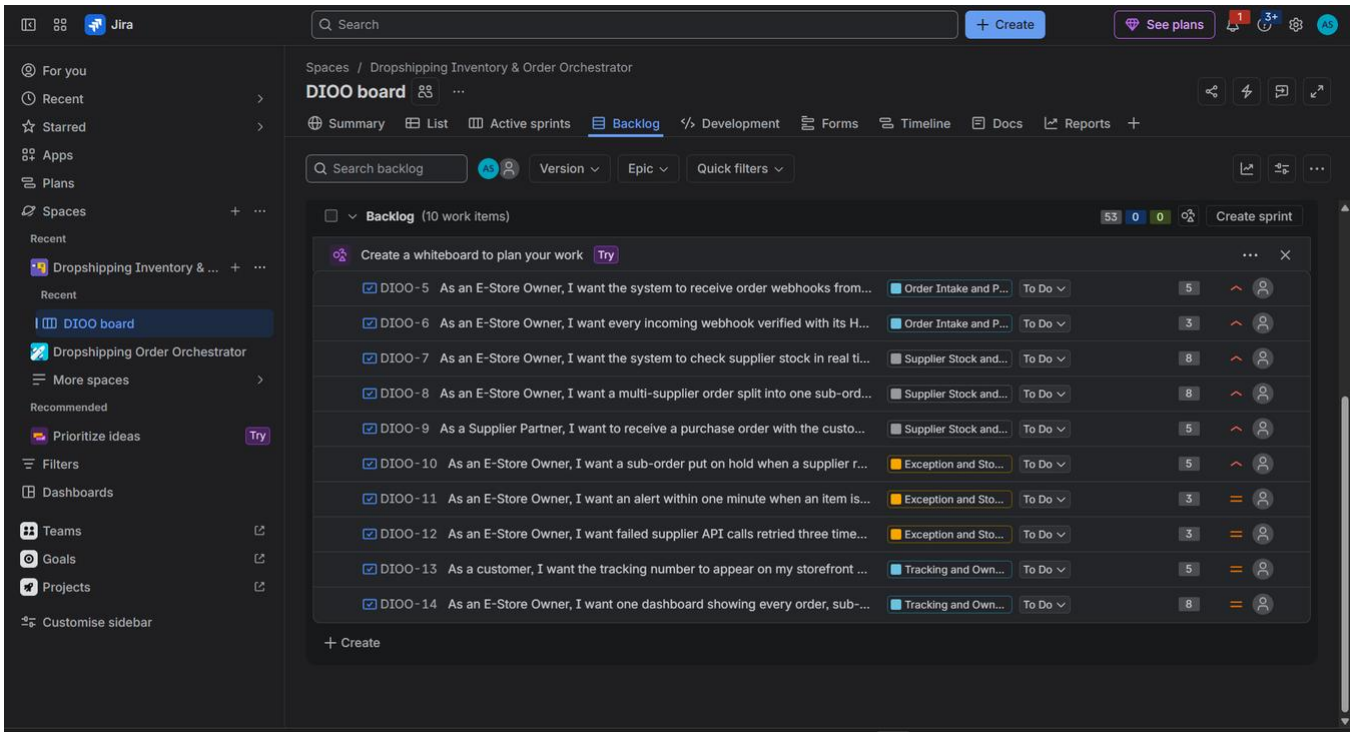


Figure 1. Product backlog with the ten User Stories, each tagged to its Epic and carrying a priority and a story point estimate.

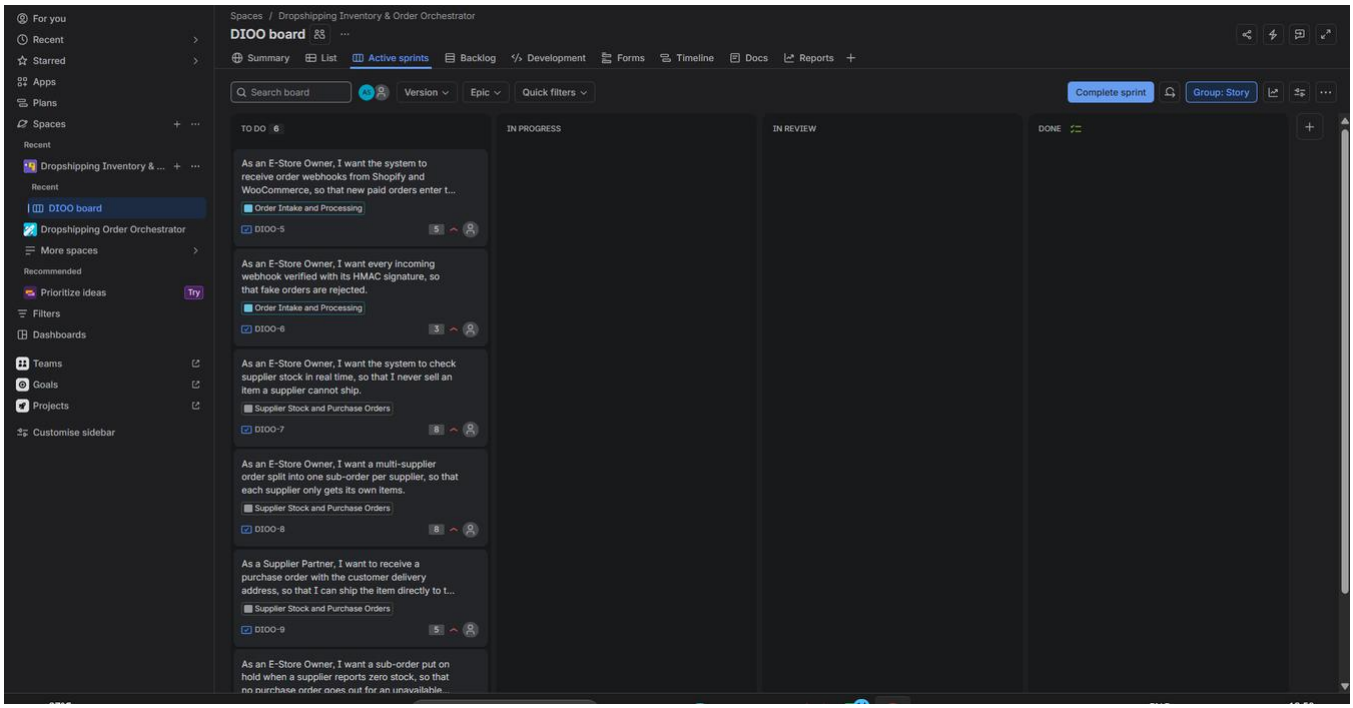


Figure 2. Active sprint board for Sprint 1, with the six committed stories in the To Do column.

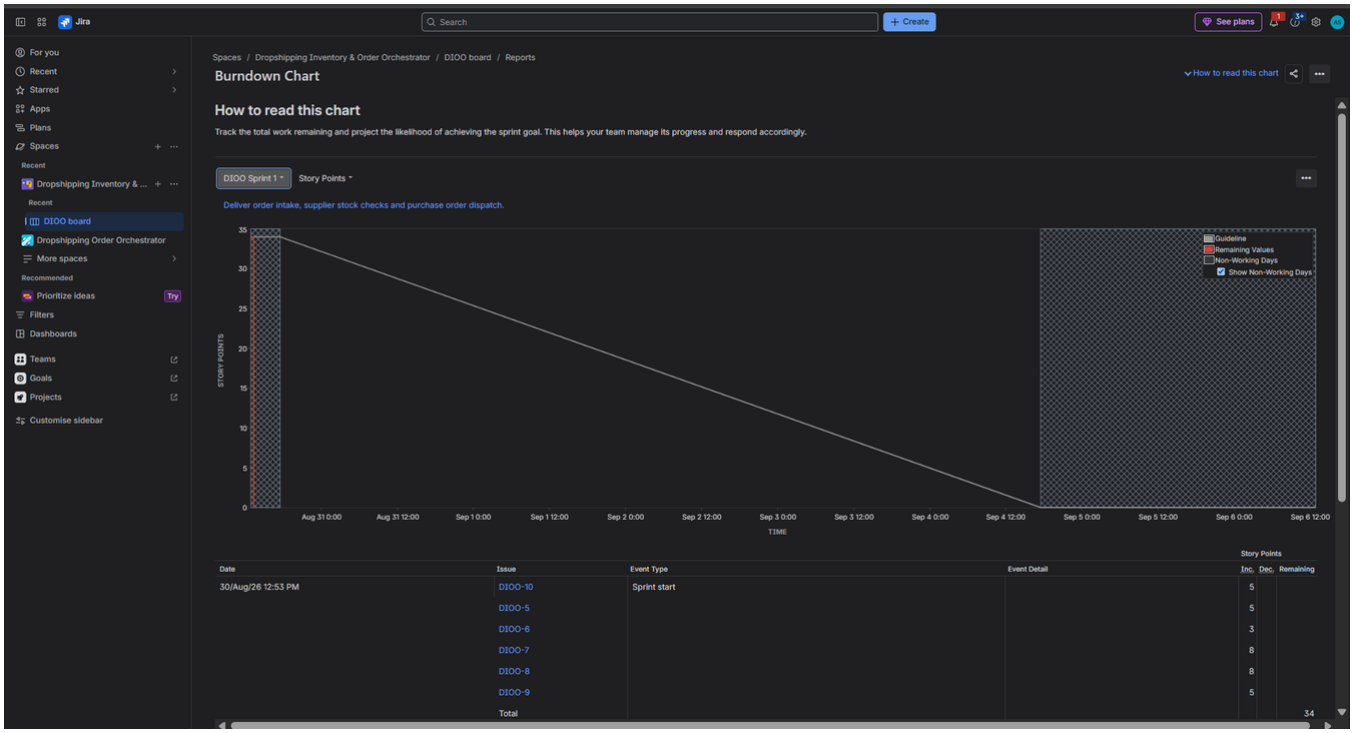


Figure 3. Burndown chart for Sprint 1, starting at 34 story points.

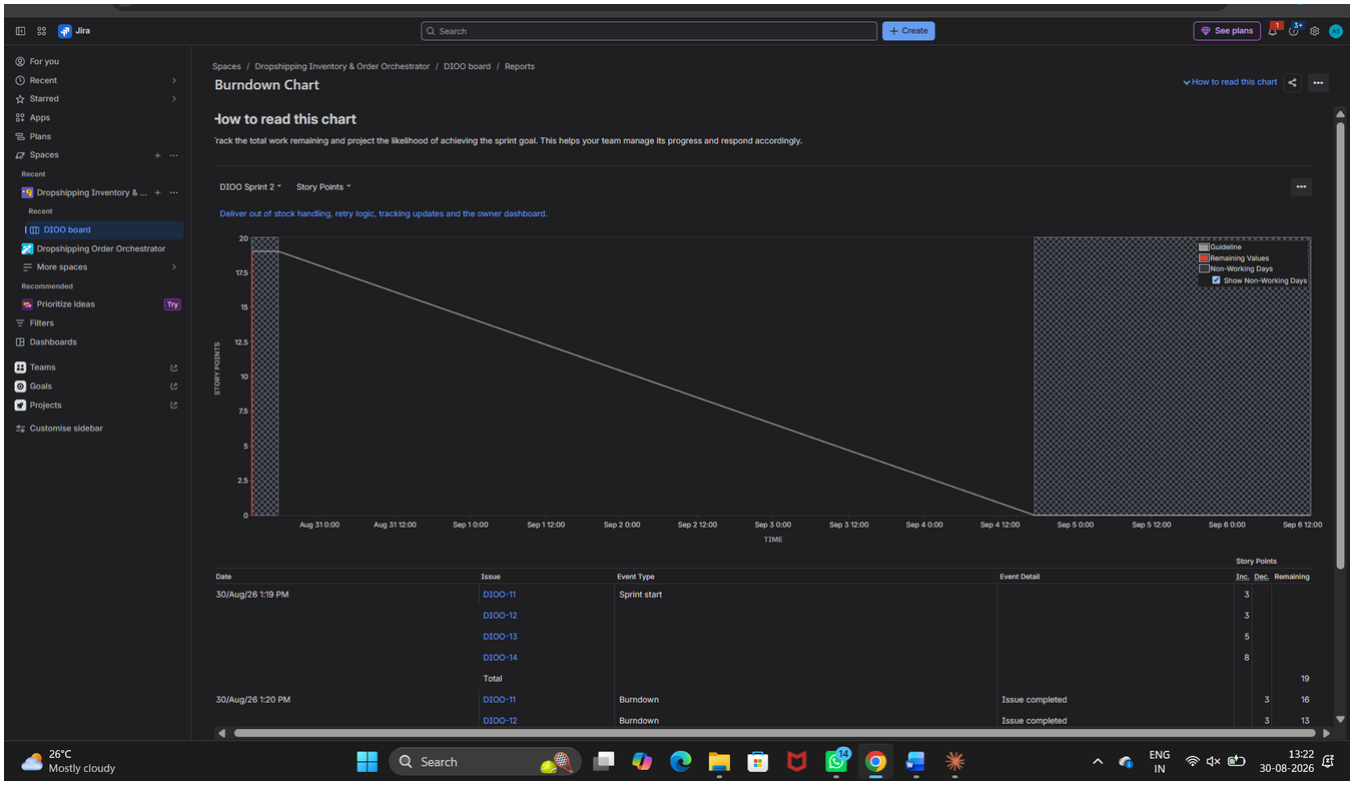


Figure 4. Burndown chart for Sprint 2, starting at 19 story points.
